

## JUDGE STEVE HERRERA JUDICIAL COMPLEX SANTA FE, NEW MEXICO

### Status for the Week of May 9, 2011

During the week of May 9, the following events took place. Forms were delivered for the walls. Pier cages were tied. Fourteen piers for the upper level were drilled, pier cages installed, and concrete poured. Grade beams for the upper level continued. A ramp was constructed to allow access to the lower level. Bulkheads were constructed along the north wall of the lower level. Rebar was tied on the ground then hoisted up and placed on the walls along the north of the lower level. Electricians started running conduit in the walls of the lower level.

### Schedule for the Week of May 16, 2011

The schedule for the week of May 16 will include the following events: Rebar will continue for the walls of the lower level with a concrete pour scheduled for Tuesday, May 17. Grade beams for the upper level will continue. The liner will be installed at the upper level west walls.



Bulkheads continue on north walls of lower level



Ramp for lower level access



Forms for walls were delivered




More forms and bulkhead construction



Installing cages and pouring concrete for drilled piers at upper level



Drilling piers at upper level

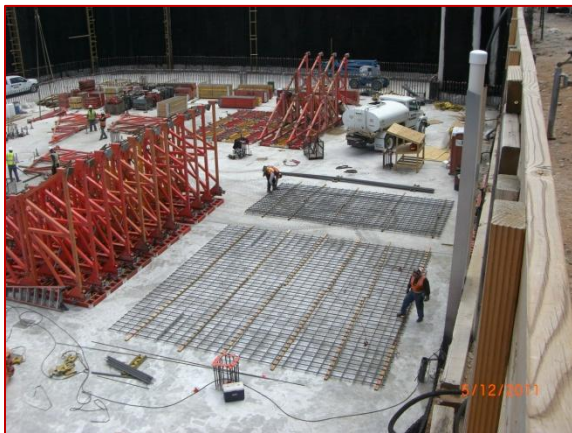

Rebar tied and forms made for north walls of lower level



Rebar hoisted up for placement at north walls of lower level; conduit being placed

This report was prepared by Sherry Keefe.

OWNER'S REPRESENTATIVE:  
Gerald A. Martin, Ltd.

*Sherry Keefe*

Sherry Keefe
