

## JUDGE STEVE HERRERA JUDICIAL COMPLEX SANTA FE, NEW MEXICO

### Status for the Week of August 1, 2011

During the week of August 1, the following events took place. Started the post-tensioning of the rods at the first level deck of the lower level parking structure. Bulkheads, rebar installation, and formwork continued at the north and west walls of the upper basement of the building. Lightning arrestors were installed every fifty feet around the perimeter of the building.

### Schedule for the Week of August 8, 2011

The schedule for the week of August 8 will include the following events: Pour concrete at perimeter of first level deck after completion of post-tensioning. Continue formwork, rebar installation, and pouring of concrete walls of upper basement of the building. Start rebar installation and formwork for walls on upper level of the parking structure.



Bulkheads and rebar on NE walls of upper basement




Rebar and formwork on NE walls of upper basement




Bulkheads, rebar, and formwork for west wall of upper basement



Bulkheads, rebar, and formwork for west wall of upper basement

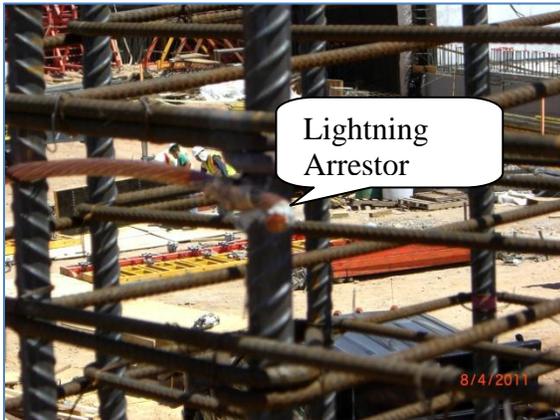

Electricians installing lightning arrestors  
at perimeter of basement

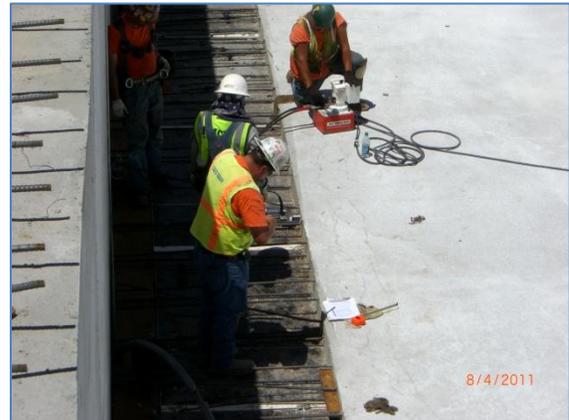

Post tensioning of rebar at first deck of  
parking structure

This report was prepared by Sherry Keefe.

OWNER'S REPRESENTATIVE:  
Gerald A. Martin, Ltd.



Sherry Keefe
