


## JUDGE STEVE HERRERA JUDICIAL COMPLEX SANTA FE, NEW MEXICO

### Status for the Week of November 21, 2011

During the week of November 21, the following events took place. Rough-in of electrical and plumbing continued. Steel erectors continued erecting steel on the building. A concrete pour took place on Wednesday morning, November 23 for the second floor north and pier caps and grade beams on the south. Fire proofing of the upper basement north continued.

### Schedule for the Week of November 28, 2011

The schedule for the week of November 28 will include the following events: Steel erectors will continue erecting steel on the building. A concrete pour for the north half of the third level of the building and the south walls is scheduled for Thursday, December 1 and the upper level ramp on Saturday, December 3. Fire proofing, fire protection, and rough-in of electrical and plumbing will continue. Masonry walls in the upper basement north will continue.

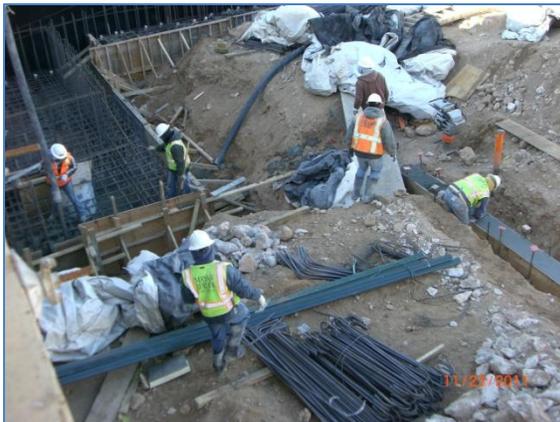

Grade beams at south building basement



Pier caps at south building basement



Fire proofing at north building basement



Concrete pour on 2<sup>nd</sup> level of building



Deck for 3<sup>rd</sup> level of building north



Ductwork arrived for install next week

This report was prepared by Sherry Keefe.

OWNER'S REPRESENTATIVE:  
Gerald A. Martin, Ltd.



Sherry Keefe
