Henry P. Roybal Commissioner, District 1

Anna Hansen Commissioner, District 2

Robert A. Anaya Commissioner, District 3



Anna T. Hamilton Commissioner, District 4

Ed Moreno Commissioner, District 5

> Katherine Miller County Manager

MEMORANDUM

DATE:

November 13, 2017

TO:

Board of County Commissioners

VIA:

Katherine Miller, County Manager

FROM:


Michael Kelley, Public Works Department Director M 11/15/17


ITEM AND ISSUE: *BCC Meeting November 28, 2017* Public Works Monthly Report for October 2017

DISCUSSION

Operations and Maintenance

Charts 1 and 2 below show our monthly work order volume. A more detailed break-out can be seen in Table 1, attached.

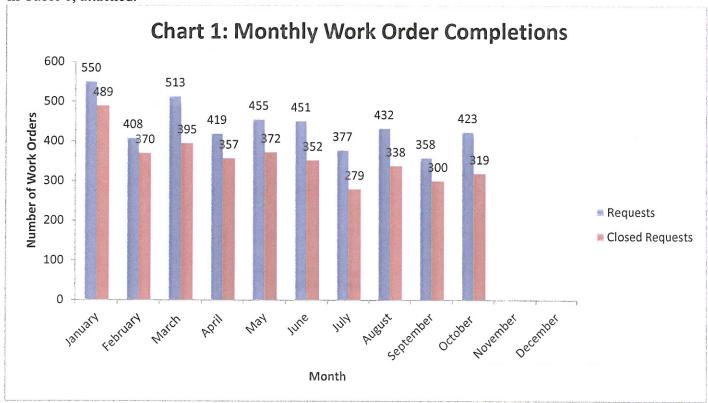

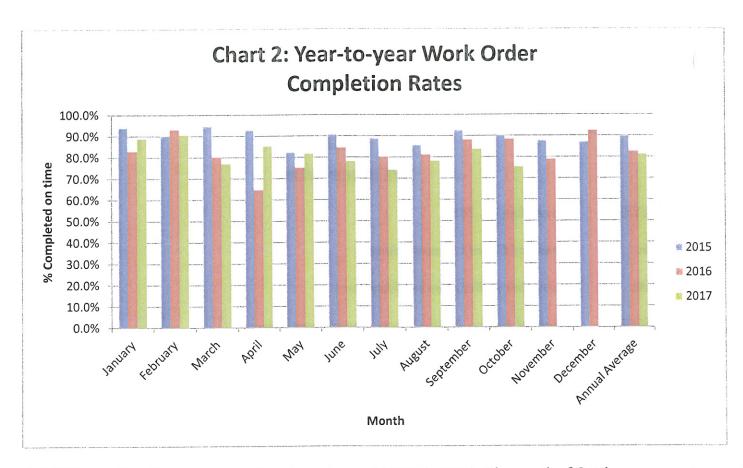

Solid Waste: The County average diversion rate was 14.32% in 2016. The month of October diversion rate was 17.03%, bringing the year-to-date average to 14.90%. See chart below.



102 Grant Avenue · P.O. Box 276 · Santa Fe, New Mexico 87504-0276 · 505-986-6200 · FAX: 505-995-2740 www.santafecountynm.gov

Solid waste permits sales are shown below.

	Number of So	olid Waste Permits Sold
Permit Type	Oct 17	CY17
1-trip	24	24
6-trip	39	393
6-trip/senior	20	191
6-trip/low income	0	0
6-trip/veteran	1	13
12-trip	127	1,494
12-trip/senior	172	1,603
12-trip/low income	2	18
12-trip/veteran	12	164
Bag tags	69	790

Utilities Division:

- SFCU participated in Pojoaque Basin Regional Water System (PBRWS) GIS Meeting with CDM Smith/Bureau of Reclamation where 30% IT/GIS support/staffing plans, key personnel roles, hardware/networking/software components, and data development needs were presented.
- Public Works staff participated in a Combined Coordination meeting held by CDM Smith/Bureau of Reclamation with PBRWS stakeholders at Buffalo Thunder Resort to present SFC interests concerning cost and project design requirements.
- Continued support of SFC growth and development by reviewing submitted construction documents for Turquoise Trails Business Park Lot Owners Association, along with conceptual plans for Arroyo Hondo and the Flying J Travel Center.
- Participated in a Water/Wastewater Utility Master Plan Progress Meeting, and a 30% review for Vista Aurora Subdivision Sewer Design.
- Met with Santa Fe Brewery to assist in wastewater pre-treatment and metering plan review. Brewery will submit plans to SFCU and SF City for comment before construction.
- SFCU invested time in a Team Meeting at Hyde Park where new employees were introduced along with a teambuilding activity, and utility plans were presented.

Project Delivery Division:

Utility Projects:

- Vista Aurora Subdivision Sewer Line Upgrade Project Manager is coordinating utility easement acquisition. Design is at 30%.
- Santa Fe County Water Reclamation Facility Proposals for design where received on November 6th. Project Team will meet on November 22nd to review proposals.
- Village of Agua Fria Waste Water Infrastructure Plan PER for water and waste water has been completed. Project Team in the process of identifying top priority projects to go out to RFP for design services.
- Antonio Lane Sewer Upgrade Design Team Kickoff Meeting was held on November 11th.
- Agua Fria Utility Corridor Design Phase. An LOI is in process for design services for Camino Maria Feliz.

Road Projects:

- Camino de Jacobo Coordinating with Housing Authority for the design and placement of elevated crosswalks and other traffic calming devices along Camino de Jacobo.
- Camino San Jose A public meeting was held on August 30. Staff is currently working on procuring drainage and roadway easements.
- CR54 Arroyo del Los Chamisos Bid Opening was held on 8/22/17, HO Construction was lowest bidder. Contract approved by BCC on September 12. Notice to proceed will be issued to contractor in November 17th.
- **NE/SE Connector** is in Phase C of The Location Study. Staff has submitted the Phase C to the NMDOT for review and approval.
- CR55A General Goodwin Rd Design Upgrade Consultant has begun redesign for 100% plans to go out for IFB for Construction. Coordinating with NMDOT for drainage easement within the railroad easement.
- Torcido Loop Chip Seal and Drainage Improvements Consultant is at 60% design. County staff is coordinating with property owners for drainage easement acquisition.
- CR89 and 89C Drainage and Roadway Improvements BCC approved the County Manager authority to purchase easement's necessary for the construction project. County staff is working on easement acquisition.
- Santa Fe Racetrack Chip Seal and Drainage Improvements Engineering consultant is under contract to begin design services.
- Glorieta Estates Chip Seal project Final ROW has been recorded. Public Meeting was held June 1st. Road Maintenance Department has begun widening the roads.
- **CR67F La Barbaria** Contract extension has been signed by Deputy County Manager. Staff has directed Engineering Consultant to provide plans to extend construction to the limits of county maintenance.
- **CR 54 Arroyo Hondo All Weather Crossing-** Engineering Consultant has been given a PO. Staff has directed Consultant to begin design of the All Weather Crossing.
- **CR 72A All Weather Crossing** Consultant has completed 60% design. Staff is working with procurement to procure engineering services though 100% design.
- Entrada La Cienega Paving has been completed. Contractor is scheduled to place base course on the shoulder November 15th.

- Alamo Lane-Curb and Gutter-Contractor completed work on October 20th, 2017.
- White Lakes Road Chip Seal Road Maintenance crews are widening the road.
- CR 12B Chip Seal Road Maintenance crews are widening the road.

Building Projects:

- Construct Improvements at County Fairgrounds & Ag Extension Office A Change Order to address added contract time and minor adjustments is in preparation. Projects is requesting cost/value analysis to add 2" rigid insulation to original block exterior walls of the building to aid in lifecycle cost and energy savings. The construction is within the project budget and contingency savings may be available to fund these Sustainability improvements.
- County Administrative Offices Projects staff is preparing a summary presentation to the BCC for commencing the Design-Build delivery method, the decision tree and the procurement of subject matter experts. Projects seeking additional experience in Design Build and Sustainability fields to assist in preparing the RFQ document for the Step 1 portion of procurement and the RFP documents for the Step 2 portion of the Design Build team selection.
- County Administrative Offices Commissioning Commissioning consultant, Matt Davis is reviewing the schematic plans and addressing any changes to EEI contract for commissioning due to the change to a Design Build delivery method.
- **District Attorney (DA) Office Remodel** Projects staff met with architect, Wayne Lloyd on 11/3/17, to discuss revisions to the current 95% completed set of Construction Documents. A meeting with the mechanical engineer is scheduled for November 9 to review and comment on proposed M&E Engineering design. Final completion of Construction Documents is scheduled after the extent of M&E improvements is confirmed.
- PW Expansion Phase II Property Control Final Construction Document delivery by Architect Allan Baer, is scheduled for November 21. The architects, representing the County, are seeking administrative approval for a variance regarding landscaping, planting and cistern requirements. The architects are also representing the County on an application for a variance from the current land use code. A secondary access road requirement is triggered by the addition of this proposed building. This variance is expected to be heard by the SFC Planning Commission.
- SFC Crises Center Scope of Work is being developed to procure design and construction services to meet requirements determined by SFC Community Services Department and a contracting services manager currently being selected by CSD. Total budget for the project is 2.2 M. Projects is providing support in coordinating alternate plan requirements for temporary CSD offices.
- Public Safety Upgrades A Stakeholder meeting to discuss the 2014 Masterplan and thoughts on current project requirements is being coordinated by the Public Safety Director.
- Chimayo Fire Station/Main The PM is procuring a survey of the property including topography. The IPR was forwarded on Monday, October 16, 2017 to the Fire Department to be entered in to the system. The PPR form requesting to hire an architect firm for the design and administration for an added apparatus bay, fitness room and storage space was forwarded to the Purchasing Division on Wednesday, September 20, 2017. Current available budget is \$250,000.00 with another \$300,000.00 through the 2016 Bond Sale. Project projected cost estimate totals \$748,733.84. Additional funding will be allocated at mid-year for construction.
- La Puebla Station #1 The PM is procuring a survey of the property including topography. An IPR was forwarded to the Fire Department on Monday, October 16, 2017 to be entered in to the system. The PM visited the site with the Fire Chief on Friday, September

- 22, 2017 and is working of a budget cost estimate and the preparation of the purchasing packet. The PPR is requesting to hire an A&E firm for the design and construction administration services for the implementation of new full time living quarters. The project budget is \$1,600,000.00. The project will be funded through the 2016 Bonds.
- Turquoise Trail Fire Station in Cerrillos An IPR was forwarded to the Fire Department on Monday, October 16, 2017 to be entered in to the system. The PPR form requesting to hire an A&E firm for the design and construction administration services for the new 3 apparatus bay unmanned fire station. The PPR was forwarded to the Purchasing Division on Wednesday, September 20, 2017. The projected project cost estimate totals \$1,453,410.00. The project will be funded \$1,600,000.00 through the 2016 Bonds.
- Ken and Patty Adam Senior Center/Max Coll Community Center Final payment to Travelers Insurance was turned in on Thursday, November 2, 2017 in the amount of \$53,774.03 on approved P.O. Travelers Insurance has made a claim for HVAC reimbursements and payment for additional Architect fees. The Architect and Engineering team responsible for the project have challenged the claim. The payment being requested is for the remainder on the original construction contract for work that has been deemed complete.
- Rancho Viejo Fire Station Staircase An IPR was forwarded to the Fire Department on Monday, October 16, 2017 to be entered in to the system. The PPR form requesting an LOI for an A&E firm for the design and construction administration services for the project was sent to the Purchasing Division on September 12, 2017. The PPR form requesting the solicitation of a contractor for the construction of the staircase was forwarded to the Purchasing Division on Wednesday, September 20, 2017. The projected project cost total is \$54,758.00 for both additional administrative services and construction of the staircase.
- Hwy 14 –Senior Community Center The Projects Division has been witnessing a steady increase in construction costs related to vertical construction in recent publically bid projects. Projects has taken measures to address cost overruns on this and other projects by requesting consulting teams provide valid updated cost projections prior to projects going to bid. The Projects Office is also working with the design team and CSD Senior Services to establish Additive or Deductive Alternates that can assist in adjusting the contractual requirements to the available budget. Several follow up meetings have been held with County Staff to discuss various alternates. The Design Team is still working on 100 % construction drawings. The certified cost estimate for the project total is \$1,668,509.00 with another \$18,466 for alternates. Current available budget is \$1,800,000.00.
- Galisteo Fire Station Remodel Construction began on Tuesday, October 31, 2017. The contractor began with the demolition of exterior block wall and site preparation. The project is scheduled to be complete within 150 days or by March 29, 2018.
- Stanley Cyclone Center The Project Manager continues to address water issues at the well. Electric controls ae required to automate this function.

 A cost proposal from Precision Electric for work needed on autofill for 30,000 gallon water storage tank is pending.
- Leo Gurule Basketball/Tennis Courts Projects received bids for this project from the Purchasing Department on October 25, 2017. Two bids were submitted and both bids exceeded the money available for this site. In consultation of the CMO it was determined not to re-bid the project and to utilize county forces to remove any hazards from the site.
- Santa Fe Mountain Center Construction Bids were received on September 28, 2017. The low lump sum bid was \$58,450.79 from Prime Builders, LLC. Purchasing is currently working on

- finalizing the contract and is routing through for required signatures. A pre-construction meeting will be scheduled once contract is finalized and a P. O. is issued.
- Bennie J. Chavez Center Septic System Upgrade A request for an IFB was forwarded to purchasing on September 25, 2017. Design Enginuity was requested to provide design and administrative services during bidding and construction of the work. A new IPR and Requisition was submitted to purchasing on October 31, 2017 in the amount of \$2500.00 for Design Enginuity services. The IFB will be advertised once the contract with Design Enginuity is finalized.
- Edgewood Senior Center ADA Upgrades A meeting with Projects staff, CSD representatives and Property Control staff was held October 23, 2017 to discuss additional improvements for the facility. The group identified additional priorities and possible solutions. A conceptual direction was established and presented to the County Manager for comment. Follow—up improvements and associated costs will be presented to the BCC on November 14, 2017.
- Edgewood Fire Station #2 Cedar Grove The final walk through was re-scheduled to verify three remaining punch list items had been addressed.
- **Jacona Collection Center** Santa Fe County is currently re-negotiating the existing lease agreement with the Jacona Land Grant Association. No further work is scheduled until land issues are resolved.

Open Space & Trails Projects:

- Santa Fe River Property Acquisition/Section B The County has closed on the Celina Paul and Gail Haggard properties. The Appraisal Reviews for the 10 properties necessary to construct the road on the North side of the River are being finalized, offers began in October. The Title Reports for the next 11 properties have been ordered. Section C- The Contract Amendment in the amount of \$15,980.00 for additional and unforeseen Cultural Resource Services has been approved.
- Santa Fe River/Frenchy's to Siler Construction KIMO's Best & Final Offer was within \$84,000 of the Counties Budget. Negotiations have been concluded. The contract has been sign and the Notice to Proceed will be issued on November 7, 2017.
- Santa Fe River/El Camino Real Design Enginuity's contract has expired, they will submit a Letter of Interest to finalize the CLOMR. The CLOMR Application Pending.
- Arroyo Hondo Trail The BCC approved a resolution on June 13, 2017 authorizing the County Manager to negotiate and to execute the purchase and sale agreements on behalf of the County necessary to acquire sufficient real property interests to construct Phase IV of the Arroyo Hondo Trail and to authorize the County Attorney to bring condemnation actions on behalf of the County to acquire the necessary real property interests in the event that the County Manager is not able to negotiate a reasonable purchase and sale agreement. The Amendment of the Easement from Rancho Viejo to allow a 10ft wide paved trail was approved by the BCC on September 26, 2017. The engineer submitted the Categorical Exclusion for the environmental certification to NMDOT on October 6, 2017. The Project Manager submitted the Agreement Request Form to NMDOT on September 28, 2017. NMDOT is requiring a full right-of-way map and title reports for all of the properties that the trail crosses even though the County already has an easement from Rancho Viejo. This will require Santa Fe County to have a survey of the Rancho Viejo Easement prepared now in order to show it on the ROW map rather than after construction is complete as stated in the easement document. The Project Manager is working with the engineer to provide the documents NMDOT has requested. Terry Lease requested quotes for the title reports. Quotes are due October 19, 2017.

- Mt. Chal The purchase agreement with the Glockhoff Trust was executed on March 9, 2017. Tierra ROW made the offer to Mr. Aitken on July 13, 2017. The BCC approved the resolution authorizing the County Attorney to bring condemnation actions on behalf of the County to acquire the necessary real property interests in the event that the County Manager is not able to negotiate a reasonable purchase and sale agreement for on July 11, 2017. INTERA submitted the VRP Application to NMED on August 10, 2017. The Project Manager conducted a site visit of the Glockhoff property with NMED on September 26, 2017. NMED issued the letter of Conditional Eligibility into the Voluntary Remediation Program (VRP) on October 16, 2016. The Project Manager submitted the legal advertisements to the newspapers for publication on October 20, 2017 for the required 30 public comment period. The public comment period ends on November 20, 2017.
- Pojoaque Sports Fields The County awarded the contract to LLR Construction at the September 12, 2017 BCC Meeting. The pre-construction conference occurred September 28, 2017. The Project Manager issued notice to proceed on October 9, 2017. The contract period is 90 calendar days. Substantial completion is expected on January 6, 2017.
- Rio Quemado Watershed Restoration The County awarded the contract to Apple Mountain Contractors on October 6, 2017. The contractor had a family emergency and is out of the state. Purchasing is holding the contract until the contractor is back in town. The contract is 60 calendar days. Substantial completion is expected in December 2017.
- Thornton Ranch Open Space The County released the draft Thornton Ranch Open Space Management Plan, Petroglyph Hill Management Plan and the Galisteo Basin Interpretive Plan for a 30 day public comment period on August 15, 2017. Staff presented the plans to COLTPAC on October 4, 2017. COLTPAC voted unanimously to recommend approval of the plans to the Board of County Commissioners. The plans were approved by the Board of County Commissioners on October 31, 2017.
- Agua Fria Monument Sign GRT funding in the amount of \$50,000 was allocated in FY 19 for construction of the monument on the west end of the village. This project is on hold until the funding is budgeted in FY 19.
- Santa Fe Rail Trail Segment 5 The Project Manager submitted the ROW Certification Request, Railroad Certification Request with a copy of the easement, ITS Project Checklist and ISA Determination to NMDOT for approval on July 19, 2017. The Project Manager submitted the Environmental LOE on August 11, 2017. The engineer submitted the 95% plans for review on August 10, 2017. The Project Manager began contacting utilities on August 17, 2017 to ensure there are no conflicts with the design for the utility certification. Purchasing sent the draft IFB to the Project Manager on September 20, 2017. The Project Manager submitted the draft IFB to NMDOT on September 25, 2017. The Project Manager submitted the CE to Purchasing for the County Manager's signature on September 14, 2017. The County Managers signed the CE on September 25, 2017. The Project Manager submitted the signed CE and all of the supporting document to NMDOT on September 28, 2017. The Project Manager submitted the Agreement Request Form to NMDOT on September 28, 2017. NMDOT approved the CE on October 16, 2017
- Santa Fe Rail Trail Segment 6 The BCC approved a Resolution granting the County Manager authority to execute the documents at the October 25, 2016 Meeting. One of the three easements was executed on December 1, 2016. Terry is working with the other two landowners to complete the easements. Santa Fe Ranchland Associates sold the property. Terry Lease is following up with the new land owner. Terry Lease requested quotes for an appraisal of the

- Commonweal easement on July 19, 2017. The purchase order was issued August 14, 2017. The completion date for the appraisal is October 24, 2017.
- El Camino Real Retracement Trail FLAP project CFLHD advertised the project for construction on September 13, 2017. The bid opening is October 12, 2017 at 2:00 PM. CFLHD received two bids. The low bid is within the construction budget. CFLHD awarded the contract on October 23, 2017.
- Santa Fe Rail Trail Trailheads The Project Manager has submitted a sole source request to Purchasing for the bidding and construction phase services. Weston submitted a revised proposal on August 30, 2017. The Project Manager is reviewing the proposal. The Project Manager reviewed the cost proposal with Weston on September 7, 2017. Weston revised and resubmitted their proposal on September 8, 2017. The Project Manager submitted a PPR and sole source request for Weston Solutions to update the plans and provide bidding and construction phase services on October 16, 2017.
- Bennie J. Chavez Community Center Park The project Manager scheduled a meeting with Planning to discuss the scope of work for the design of the park on July 5, 2017. The Project Manager held a meeting with County staff to discuss the current use and condition of the Community Center facilities and the vision for the future of the facilities in order to develop a scope of work for the park renovations. The Project Manager will work with planning to set up a meeting with key community stakeholders to discuss the scope of work for the park. The Project Manager requested recommendations from the County Planning staff for community members to serve on a steering committee for the project on September 6, 2017.
- Pojoaque Valley Recreation Complex Phase III The Project Manager submitted a PPR for Phase II on August 24, 2017. The RFP was assigned to Mari Martinez. GRT funding in the amount of \$248,000 was allocated for Phase III on August 28, 2017. Purchasing sent the draft RFP to the Project Manager for review on October 2, 2017. Proposals are due November 27, 2017. Projects plan to award the contract in December 2017.
- Romero Park Phase II Purchasing advertised the RFP on September 10 & 11, 2017. The Pre-Proposal Meeting was held September 19, 2017. Addendum No. 1 was issued September 28, 2017. Proposals are due October 26, 2017. The Evaluation Committee meeting is scheduled for November 6, 2017. Plan to award the contract in November 2017.

ACTION REQUESTED:

None; for information only.

Table 1: October 2017 Work Order Report

Property Control

116

TOTAL

Property Contro				
				WORK
				ORDER
			WORK	ISSUE
			ORDER	ASSESSED
COMM. DIST.	REQUESTS	ISSUED	CLOSED	ON TIME
1	17	17	13	8
2	6	6	6	6
3	11	11	9	9
4	24	23	19	22
5	14	14	8	11
All	44	44	35	40

115

99.14%

90

77.59%

96

82.76%

			WORK
			ORDER
		WORK	ISSUE
		ORDER	ASSESSED
REQUESTS	ISSUED	CLOSED	ONTIME
3	3	3	3
0	0	0	0
0	0	0	0
2	2	2	1
3	3	3	2
19	19	19	19
27	27	27	25
	100.00%	100.00%	92.59%
	3 0 0 2 3 19	3 3 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	REQUESTS ISSUED CLOSED 3 3 3 3 0 0 0 0 0 0 0 0 2 2 2 2 3 3 3 3 19 19 19 19 27 27 27

		33.1470	17.5570	02.7070		- 1		1	100.00%	100.00%	92.59%
Roads	7	7					Open Space		*******************************	L	
									***************************************		WORK
		Overall WO			On-time	- 1					ORDER
	Overall WO's	Issued from	Closed from	Request	request	- 1				WORK	ISSUE
	from public &	public &	public &	from public	from public					ORDER	ASSESSED
COMM. DIST.	staff	staff	staff	only	only		COMM. DIST.	REQUESTS	ISSUED	CLOSED	ON TIME
1	38	38	31	38	31		1	21	11	9	9
2	5	5	5	5	5		2	20	11	8	8
3	26	26	22	17	13		3	22	16	14	13
4	52	52	52	13	13	П	4	10	8	5	5
5	19	19	14	16	11		5	10	8	6	6
All	4	4	4	0	0		All .	15	6	5	5
TOTAL	144	100	420			_					
TOTAL	144	144	128	89	73		TOTAL	98	60	47	46
		100.00%	88.89%		82.02%	- 1			61.22%	47.96%	46.94%

ic	-	p-1			
	Overall WO's from public &			Request from public	On-time request from public
COMM. DIST.	staff	staff	staff	only	only
1	10	10	4	4	3
2	4	4	4	0	0
3	13	13	10	3	1
4	2	2	2	0	0
5	. 3	3	2	0	0
All	6	6	5	1	1
TOTAL	38	38	27	8	5
		100.00%	71.05%		62.50%



Capital Project Status Update (As of 11/8/2017 10:46:47 AM)

Page 1 of 5	Ded C				0.00	i	1		000	Dowleign.
Joseph Martinez	11/30/2017	9/20/2017	\$4,000.00	2%	\$160,447.00	12345	75	Design	Women's Health Building HVAC Upgrades	0775
Brad Isaacson	12/29/2017	4/20/2017	\$1,040,939.85	%59	\$1,600,000.00	12345	35	Construction	Ag Extension Office	0759
Ron Sandoval	6/29/2018	9/15/2017		%0	A Land A Construction of the production of the construction of the	and yet it get the production and the second production that the second testing of the second	0	Design	La Puebla Station #1	8031
Ron Sandoval	5/29/2018	9/15/2017	A PERSONAL PROPERTY OF THE PRO	%0	\$550,000.00	The state of the state by the state of the s	O	Design	Chimayo Fire Station - Main	8020
Colleen Baker	12/1/2018	12/1/2017	The second secon	%0	\$24,000.00	enque i desente en material de Austria de Carlo	The state of the s	Design	Bennie J. Chavez Park	7712
Russell Naranjo	5/18/2018	3/15/2018		%0	\$100,000.00	The second secon	0	Design	Abedon Lopez Remodel	7711
Justin Reese	11/17/2017	4/26/2017	\$76,707.25	31%	\$250,000.00	eren Jahren der eiler Franzischer gericht ertran	09	Design	Bridge Rebuild on CR72A	6217
Shannon Vigil	1/31/2018	12/14/2015	\$121,208.60	100%	\$121,208.60	The second of th	06	Acquisition	Programming for Drainage and Roadway Improvements on County Road 89 C	6199
Shannon Vigil	9/30/2018	5/17/2017		%0	\$515,000.00	_	The second secon	Acquisition	Drainage and Roadway improvements on County Road 89	6198-2
Joseph Martinez	12/28/2018	1/24/2018		%0	\$2,038,000.00	~	10	Construction	Jacona - Northern Santa Fe County Solid Waste Convenience Center	6190
Erik Aaboe	6/30/2018	6/1/2016	\$46,600.00	10%	\$482,656.00	~	25	Acquisition	Chupadero Acquisition	1477
Colleen Baker	1/31/2018	11/20/2017	\$100,523.95	86%	\$117,152.00	The second secon	6	Construction	Rio Quemado Watershed Restoration Phase II	1472
Erik Aaboe	1/1/2018	8/1/2016	\$625,000.00	100%	\$625,000.00	~	2	Construction	Cuatro Villas MDWUA Waterline	1468
Erik Aaboe	9/30/2018	8/1/2016	\$625,000.00	100%	\$625,000.00	-	06	Construction	Greater Chimayo MDWCA Waterline	1464
Russell Naranjo	12/29/2017	12/4/2017		%0	\$100,000.00		0	Design	Marcos Trujillo Remodel	0764
Joseph Martinez	1/26/2018	12/18/2017		%0	\$50,000.00		10	Construction	Bennie J Chavez Septic System	0755
Colleen Baker	1/31/2018	10/9/2017	\$400,298.37	82%	\$487,032.33	-	_	Construction	Construct Pojoaque Valley Recreation Complex Phase II	0736
Colleen Baker	12/31/2018	12/18/2017	national hadronical horizon	%0	\$91,632.00	~	5	Design	Pojoaque Valley Recreation Complex Phase III	0736
Joseph Martinez	3/30/2018	10/30/2017	ni verrinde e d	%0	\$15,000.00	-	9	Design	Tesuque Retaining Wall	
Ron Sandoval				%0	\$48,140.00			Design	Eldorado Fire #4	8022
Project Manager	Estimated Completion Date	Estimated Start Date	Current Contract Amount	Over/ Under	Project Budget	District	dwo2	Nature of Procurement	Project Name	PW ProjectNbr



Capital Project Status Update (As of 11/8/2017 10:46:47 AM)

was a substant of the substant																				
Project Manager	David Madrid	Brad Isaacson	Brad Isaacson	Brad Isaacson	Brad Isaacson	Brad Isaacson	Russell Naranjo	Chris White	Brad Isaacson	Derrek Garcia	Justin Reese	Colleen Baker	Joseph Martinez	Joseph Martinez	Joseph Martinez	David Madrid	David Madrid	David Madrid	David Madrid	David Madrid
Estimated Completion Date	12/1/2018	10/18/2017	8/12/2019	9/5/2022	12/20/2017	12/15/2017	3/31/2017	9/30/2018	7/1/2019		3/31/2018	12/31/2018	3/15/2018	12/29/2017	11/30/2017	3/30/2018	1/17/2018	3/30/2018	1/31/2018	
Estimated Start Date	3/1/2018	1/21/2017	3/24/2016	3/11/2016	8/24/2016	10/24/2017	12/1/2017	8/15/2017	12/4/2017		12/1/2017	12/11/2017	11/16/2017	10/23/2017	10/23/2017	1/2/2018	9/8/2016	11/8/2017	9/7/2017	2/5/2018
Current Contract Amount		\$139,733.92	\$2,167,083.31	\$270,701.15	\$127,873.00	\$56,773.08					\$64,336.63		\$63,750.00	\$108,081.00	\$100,000.00	\$4,900.00	\$159,687.00	\$41,842.00	\$45,160.00	
Over/ Under	%0	100%	%66	%86	%86	%96	%0	%0	%0	%0	%8	%0	85%	100%	100%	10%	100%	84%	32%	%0
Project Budget	\$800,000.00	\$139,733.92	\$2,200,000.00	\$275,000.00	\$130,000.00	\$60,000.00	\$50,000.00	\$245,387.00	\$2,200,000.00	\$60,000.00	\$799,759.00	\$213,646.00	\$75,000.00	\$108,081.00	\$100,000.00	\$50,000.00	\$160,000.00	\$50,000.00	\$141,826.00	\$1,000,000.00
District	12345	12345	12345	12345	12345	12345	12345	12345	12345	13	2	2	2	2	2	2	2	2	2	2
% Comp	1	95	33	25	95	85	O STANLAND AND AND AND AND AND AND AND AND AND	0	0		7	7	10	10	10	Ю	66	Ю	30	0
Nature of Procurement	Design	Design	Other	Design	Design	Design	Construction	Construction	Design	Construction	Construction	Design	Construction	Construction	Construction	Design	Plan	Design	Design	Plan
Project Name	County Water Reclamation Facility	Adult Detention Facility Master Plan	County Administrative Offices / A/E	County Administrative Offices -	Public Works Expansion PH II - Property Control bldg.	District Attorney Complex ADA & Office Upgrades	Admin Building Window Refurbish	Solarize County Facilities	Santa Fe County Crisis Center	PWD Secondary Containment Structures	Pinon Hills AWC	Romero Park Phase II	Santa Fe Mountain Center Renovation	Women's Health Electrical	Women's Health Building - Parking Lot resurfacing	Camino Maria Feliz Sewer Line	Agua Fria Utilites Plan (PER) PHASE II Plan	Antonio Lane Sewer Upgrade	Vista Aurora Sewer System	Village of Agua Fria Wastewater Infrastructure
PW ProjectNbr	1473	1860	2219	2219	6208	7123	7124	7127	7129	8090	9990	0732	9920	0775	0775	1443	1444	1459	1489	1492
T.	21	22	23	24	25	26	27	28	29	30	31	32	33	34	35	36	37	38	39	40

7 10:46:47 AM	Value of the same
11/8	
Time:	
1.0.0	
Revision:	

Page 2 of



Capital Project Status Update (As of 11/8/2017 10:46:47 AM)

Page 3 of 5	Pa			_	11/8/2017 10:46:47 AM	Time: 11/8	F		1.1.0.0	Revision:
Scott Smith	12/31/2017	10/27/2017	\$63,293.85	11%	\$562,141.75	8	2	Design	Upgrade Kace Track Subdivision Chip Seal	6207
Scott Smith	9/30/2018	12/1/2017	the second secon	%0	\$250,000.00	S and the second	5	Construction	Simmons Road CR 26	6196
Scott Smith	9/30/2018	7/19/2017		%0	\$500,000.00	က	2	Construction	B Anaya Road CR 12B	6193
Scott Smith	12/31/2017	6/1/2017	\$157,291.41	13%	\$1,189,437.97	To an address of the control of the	30	Design	Torcido Loop - Design/Archaeological Survey	6183
Shannon Vigil	1/31/2018	9/23/2013	\$233,316.97	100%	\$233,316.97	က	20	Design	CR 55A General Goodwin Rd Design Upgrade	6182
Scott Smith	12/1/2017	11/20/2017	\$43,259.83	%26	\$44,690.74	ဇ	2	Construction	CR50F - Entrada La Cienega Shoulder Project	6171
Shannon Vigil	4/1/2018	11/24/2017	\$932,135.48	100%	\$932,135.48	က	2	Construction	Los Pinos Road AWC at Arroyo de los Chamisos	6167
Justin Reese	12/8/2017	7/17/2017	\$186,727.27	100%	\$186,727.27	က	15	Design	Los Pinos Road AWC at Arroyo Hondo	6167
Shannon Vigil	3/31/2018	10/10/2014	\$87,220.76	100%	\$87,220.76	3	20	Plan	Upgrade County Road 50A - Camino San Jose	6159
Joseph Martinez	9/13/2017	6/1/2017	\$40,000.00	24%	\$163,721.00	ю	92	Construction	Edgewood Senior Center ADA Improvements	0737
Russell Naranjo	3/30/2018	3/1/2018	Andrew V Parl Page 1	%0	\$65,807.00	က	0	Construction	La Cienega Community Center Parking Lot	0711
Joseph Martinez	3/30/2018	10/30/2017		%0	\$40,000.00	က	2	Plan	Edgewood #3	
Joseph Martinez	2/2/2018	10/30/2017		%0	\$30,000.00	8	2	Plan	Turquoise Trail #2	A CONTRACTOR AND A CONT
Colleen Baker	1/31/2019	6/10/2015	\$4,394,170.41	100%	\$4,396,000.00	2, 3	20	Other	Design and Construct El Camino Real Buckman Road Segment Retracement Trail	7733
Russell Naranjo	3/30/2018	12/4/2017		%0	\$117,000.00	2	Ŋ	Plan	Agua Fria Station #1	8027
Scott Kaseman	10/31/2018	11/27/2017	\$15,980.00	100%	\$15,980.00	2	09	Acquisition	Santa Fe River Greenway Acquisition of BLM Parcels in Section "C"	7708
Scott Kaseman	12/29/2017	10/3/2012	\$340,633.57	83%	\$412,725.85	2	86	Design	Santa Fe River Greenway Design - El Camino Real	7708
Scott Kaseman	11/17/2018	11/17/2017	\$4,079,064.46	91%	\$4,461,900.00	2	10	Construction	Santa Fe River Greenway - Frenchy's Field to Siler Bridge	7708
Scott Kaseman	11/8/2018	11/8/2016	\$336,920.00	22%	\$1,551,920.00	2	35	Acquisition	Santa Fe River Greenway "B" Acquisitions	7708
Derek Garcia		1/2/2018		%0	\$206,900.00	2	0	Construction	Camino de Jacobo Microsurfacing	6220
Project e Manager	Estimated Completion Date	Estimated Start Date	Current Contract Amount	Over/ Under	Project Budget	District	dmo2	Nature of Procurement	Project Name	PW ProjectNbr



Capital Project Status Update (As of 11/8/2017 10:46:47 AM)

Project Manager	ith	ith	iff	doval	doval	3aker	3aker	doval	doval	lartinez	Jartinez	Jaranjo	/artinez	ese	90)e	arcia	arcia	rcia	Jaranjo
	Scott Smith	Scott Smith	Scott Smith	Ron Sandoval	Ron Sandoval	Colleen Baker	Colleen Baker	Ron Sandoval	Ron Sandoval	Joseph Martinez	Joseph Martinez	Russell Naranjo	Joseph Martinez	Justin Reese	Erik Aaboe	Erik Aaboe	Derrek Garcia	Derrek Garcia	Rudy Garcia	Russell Naranjo
Estimated Completion Date	9/30/2018	9/30/2018	9/30/2018	12/29/2017	10/30/2017	12/31/2017	6/30/2019	4/30/2018	5/30/2018	3/30/2018	9/15/2017	11/30/2017	3/30/2018	11/24/2017	9/30/2019	3/30/2018	10/1/2018	10/1/2018	aud per halt den in erman sosjeller i hersalfrögen optiv syklepsammin konstru	12/31/2017
Estimated Start Date	11/13/2017	7/19/2017	11/13/2017	12/18/2015	9/26/2016	8/1/2012	11/1/2017	9/29/2017	9/15/2017	10/30/2017	6/1/2017	11/13/2017	10/30/2017	9/20/2017	12/30/2018	8/25/2015	7/1/2018	7/1/2018	generalis (1) (1447) (A) (400) (1) 440) (1) 440 mg/mm/mm/mm	9/29/2017
Contract Amount	And a state of the	The state of the s		\$2,926,540.13	\$136,473.75	\$74,467.69		\$457,157.00		es al estado	\$26,100.00	The state of the s	The second section of the section of th	\$26,750.00	The second secon	\$19,496.00		\$5,123.18	\$50,000.00	
Over/ Under	%0	%0	%0	103%	%9	%8	%0	100%	%0	%0	40%	%0	%0	100%	%0	17%	%0	3%	100%	%0
Project Budget	\$270,000.00	\$1,350,000.00	\$750,000.00	\$2,848,500.00	\$2,100,000.00	\$988,499.00	\$200,000.00	\$457,157.00		\$140,780.00	\$65,000.00	\$50,000.00	\$50,000.00	\$26,750.00	\$758,177.00	\$115,000.00	\$168,156.00	\$200,000.00	\$50,000.00	\$25,000,000
District		က	က	က	က	က	က	က	က	က	3	က	4	4	4	4	4	4	4	_
% Comp	2	2	2	92	95	70		0	0	5	95	7	5	30	Ŋ	85	25	5	O	C
Nature of Procurement	Construction	Construction	Construction	Construction	Design	Acquisition	Design	Construction	Design	Design	Construction	Construction	Plan	Design	Acquisition	Acquisition	Construction	Construction		201
Project Name	Drake Road CR 9A	White Lakes Rd CR 20B	King Farm Road CR 21	Stanley Cyclone Center Arena	Highway 14 Senior/Community Center	Mt. Chalchihuitl	Thornton Ranch Open Space Master Plan Implementation	Galisteo Fire Station Remodel	Turquoise Trail Fire Station in Cerrillos	Madrid Fire Station Expansion	Edgewood Fire Station #2/Cedar Grove (1)	Stanley Fire Station #3 Roof	Eldorado Station #2	Road Safety Audit @ Rabbit Rd.	Acquisition Canoncito Water System	Acquisition Hyde Park Estate Water System	Camino Pacifico	Glorieta Estates	Glorieta Civil War Memorial	otolicael acital Coult
PW ProjectNbr	6221	6223	6224	7121	7122	27706	7711	8013	8015	8016	8017	8023		0601	1484	1485	6212	6215	7128	0000
<u>o</u>	61	62	63	64	65	99	29	68	69	70	71	72	73	74	75	92	11	78	79	C

e: 11/8 '10:46:47 AM	
Time:	
Revision:	

Page 4 of



Capital Project Status Update (As of 11/8/2017 10:46:47 AM)

PW ProjectNbr	Project Name	Nature of Procurement	% Comp	District	Project Budget	Over/ Under	Current Contract Amount	Estimated Start Date	Estimated Completion Date	Project Manager
9695	CR67F La Barbaria Drainage and Road Paving Design	Design	20	4	\$199,780.55	100%	\$199,780.55	3/14/2016	2/1/2018	Shannon Vigil
7707	Santa Fe Rail Trail Trailheads	Design	6	4,5	\$20,000.00	%0	the Charles Super-Ventor Constitution (1998) and Charles Super-Ventor (1998) and Charles	12/18/2017	6/30/2019	Colleen Baker
0150	Public Safety Complex Upgrade	Design	2	2	\$50,000.00	84%	\$42,188.00		9/21/2018	Brad Isaacson
9690	Avenida Amistad Paving	Construction	10	2	\$100,000.00	2%	\$4,989.30	10/23/2017	11/30/2017	Justin Reese
0753	Solarize Ken & Patty Adam Senior Center	Construction	0	2	\$100,000.00	%0		11/13/2017	1/15/2018	Chris White
0753	Construct Addition to Ken & Patty Adam Senior Center	Construction	66	2	\$1,456,963.00	94%	\$1,363,302.84	8/18/2014	12/29/2017	Ron Sandoval
0832	Rancho Viejo Fire - Loft Access	Construction	0	5	\$55,000.00	%0		11/30/2017	3/15/2018	Ron Sandoval
6181	NE-SE Connectors Location Study	Plan	95	5	\$500,000.00	100%	\$499,999.23	2/4/2013	1/1/2018	Justin Reese
7701	Arroyo Hondo Trail	Design	09	2	\$470,572.00	%26	\$458,569.23	12/13/2012	5/31/2018	Colleen Baker
7707	Santa Fe Rail Trail Segment 5	Design	95	2	\$40,000.00	81%	\$32,400.00	3/8/2017	3/31/2018	Colleen Baker
7077	Acquire Santa Fe Rail Trail Segment 6 Acquisition	Acquisition	30	5	\$55,747.47	%1	\$3,852.00	3/15/2016	12/31/2017	Colleen Baker
7724	Leo Gurule Basketball Court	Construction	10	Ŋ	\$80,000.00	%0		11/13/2017	12/29/2017	Joseph Martinez

Revision: 1.1.0.0

Time: 11/8

11/8/2017 10:46:47 AM
